



LAB 2

SRN: PES1UG24CS421
NAME: SANJANA S AITHAL

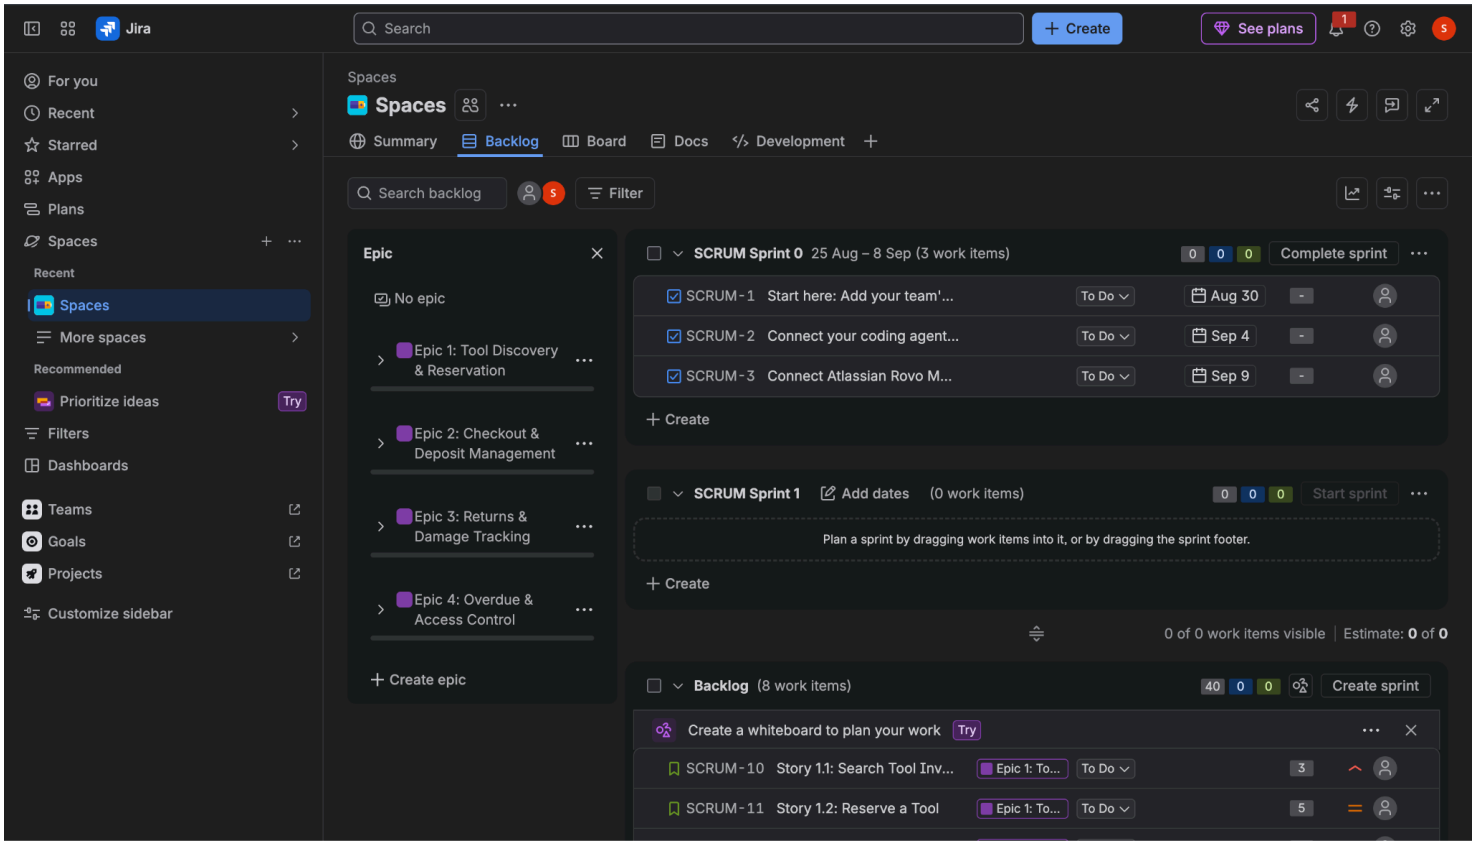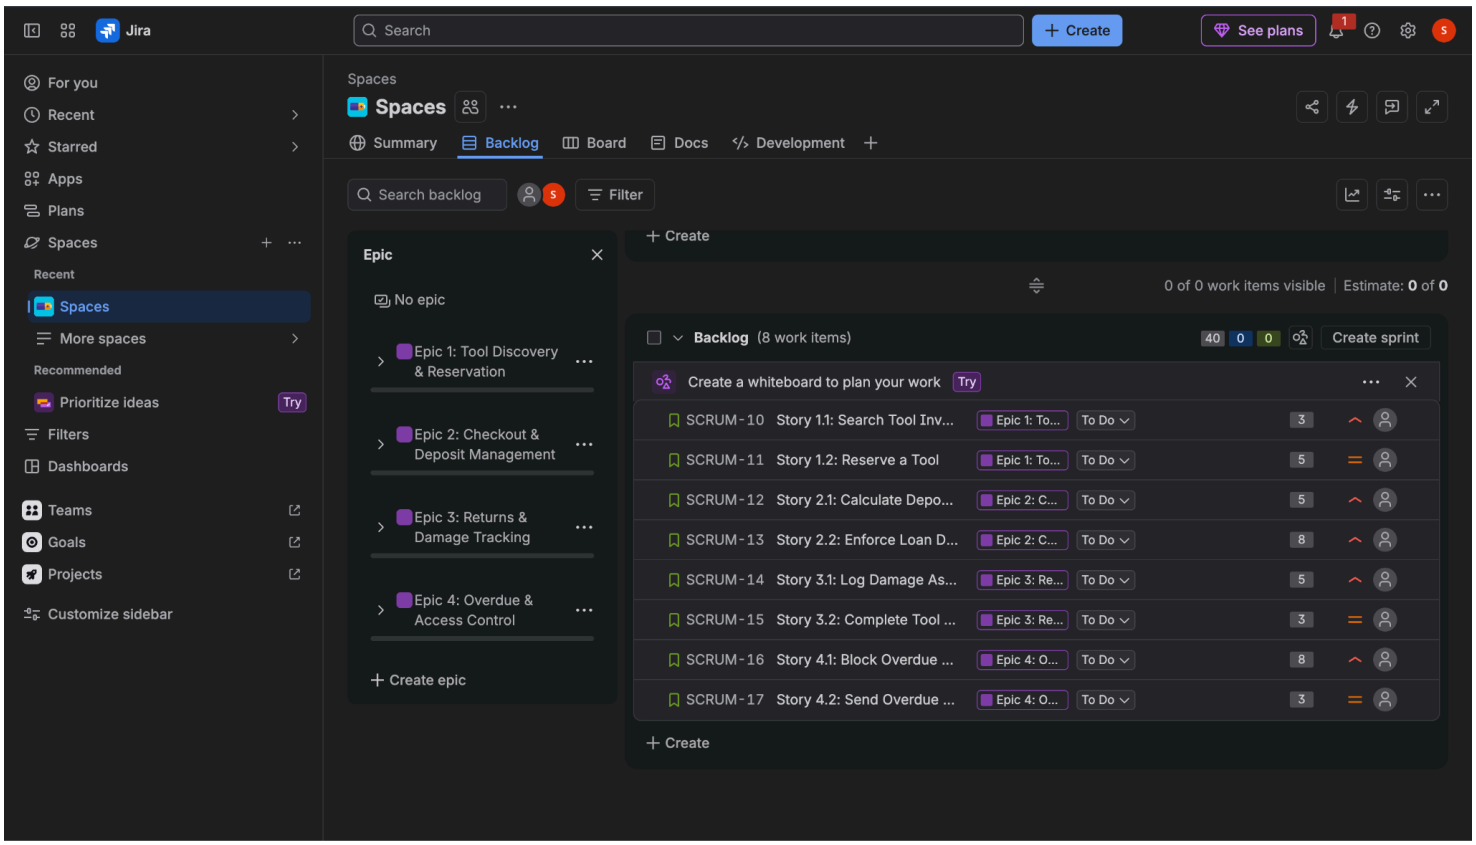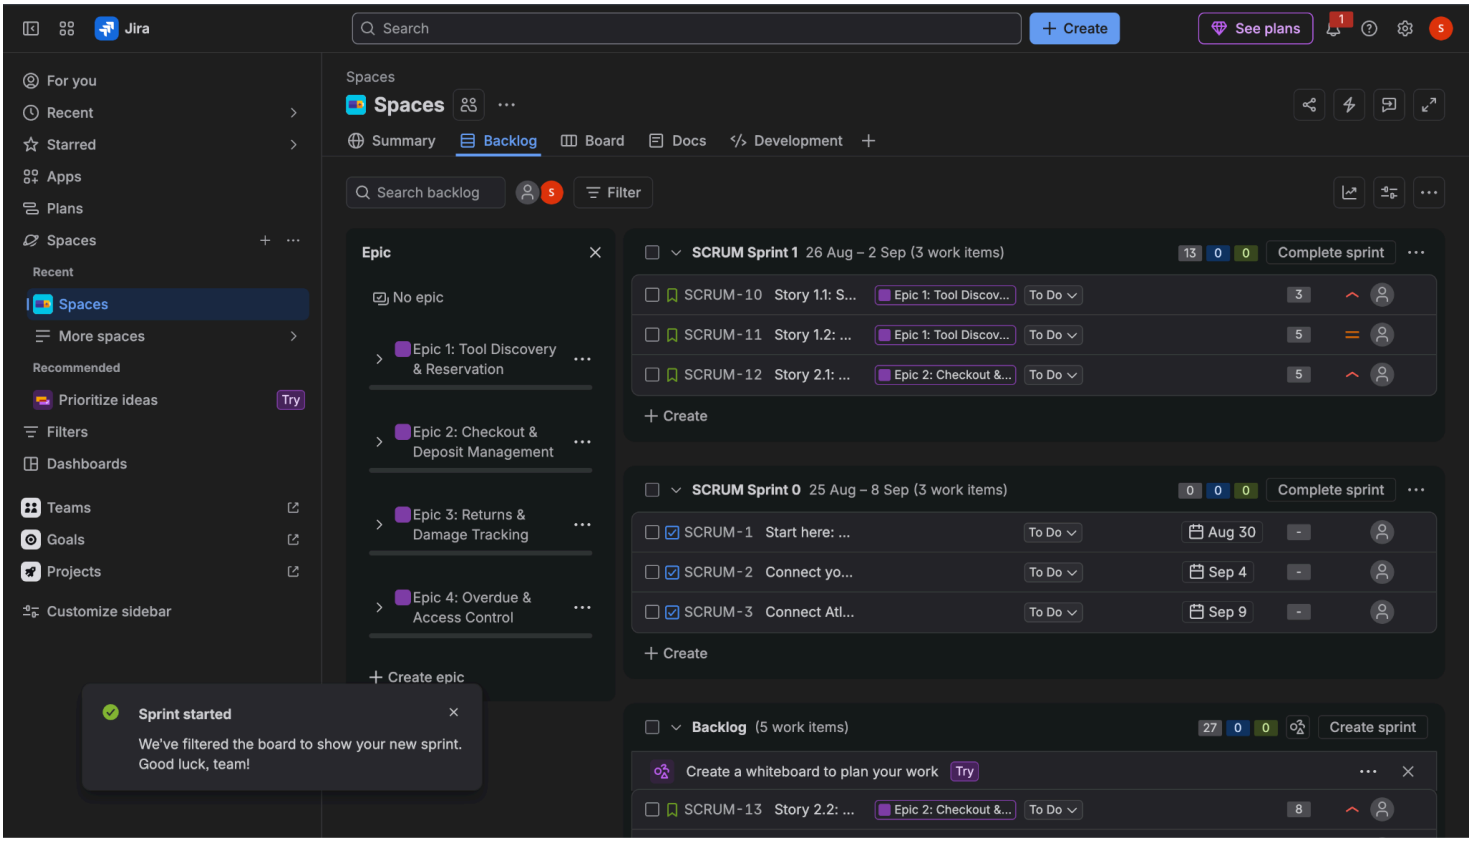

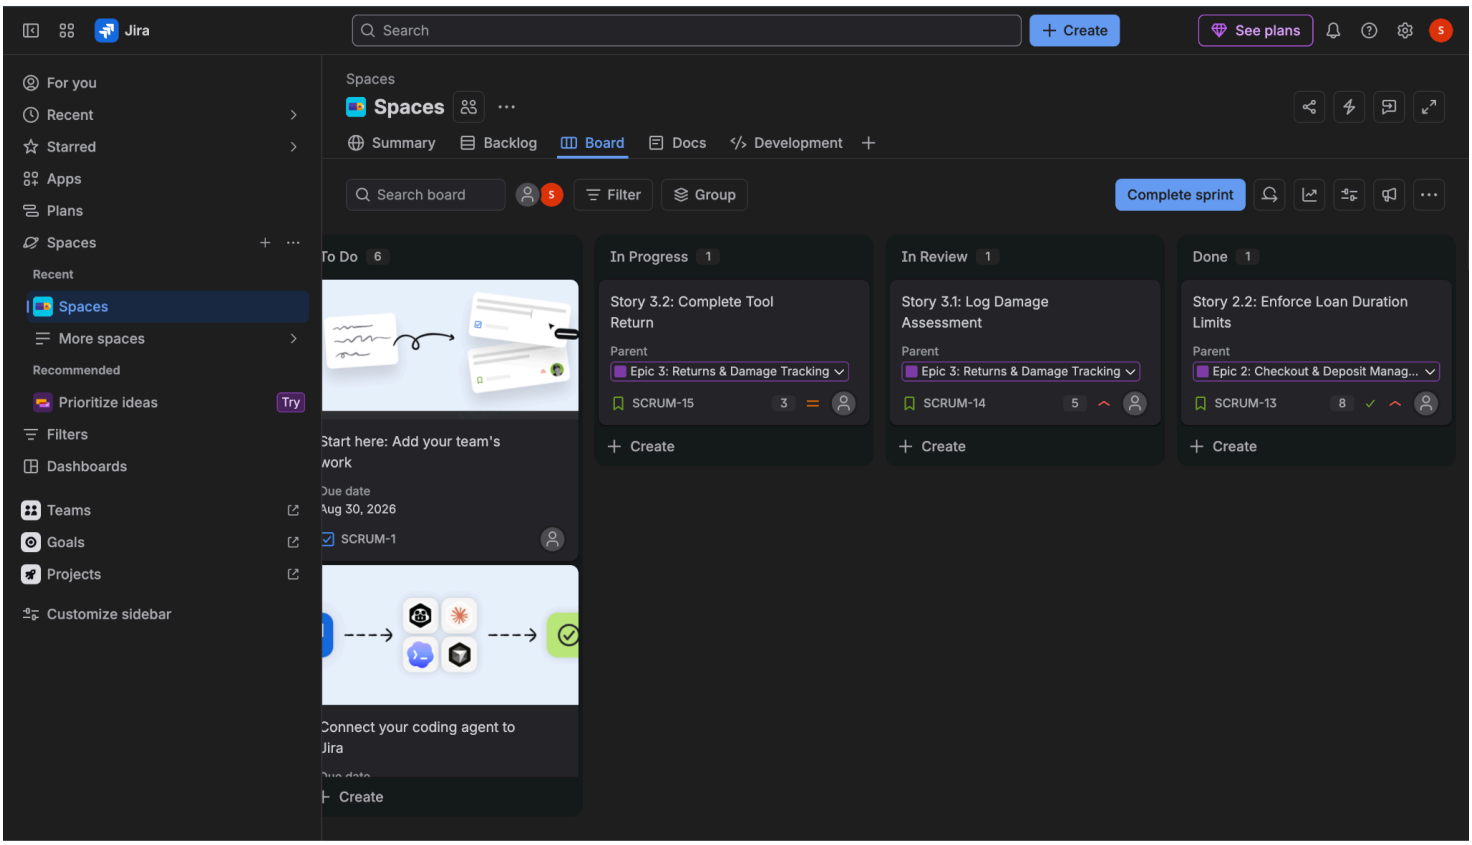


Jira
Search
Create
See plans
For you
Recent
Starred
Apps
Plans
Spaces
Recent
Spaces
More spaces
Recommended
Prioritize ideas
Try
Filters
Dashboards
Teams
Goals
Projects
Customize sidebar
Spaces
Spaces
Summary
Backlog
Board
Docs
Development
Search backlog
Filter
Epic
No epic
Epic 1: Tool Discovery & Reservation
Epic 2: Checkout & Deposit Management
Epic 3: Returns & Damage Tracking
Epic 4: Overdue & Access Control
Create epic
SCRUM Sprint 1 26 Aug – 2 Sep (3 work items)
Complete sprint
SCRUM-10 Story 1.1: S... Epic 1: Tool Discov... To Do
SCRUM-11 Story 1.2: ... Epic 1: Tool Discov... To Do
SCRUM-12 Story 2.1: ... Epic 2: Checkout &... To Do
Create
SCRUM Sprint 0 25 Aug – 8 Sep (3 work items)
Complete sprint
SCRUM-1 Start here: ... To Do Aug 30
SCRUM-2 Connect yo... To Do Sep 4
SCRUM-3 Connect Atl... To Do Sep 9
Create
Sprint started
We've filtered the board to show your new sprint. Good luck, team!
Backlog (5 work items)
Create sprint
Create a whiteboard to plan your work
Try
SCRUM-13 Story 2.2: ... Epic 2: Checkout &... To Do


Jira
Search
Create
See plans
For you
Recent
Starred
Apps
Plans
Spaces
Recent
Spaces
More spaces
Recommended
Prioritize ideas
Try
Filters
Dashboards
Teams
Goals
Projects
Customize sidebar
Spaces
Spaces
Summary
Backlog
Board
Docs
Development
Search board
Filter
Group
Complete sprint
To Do 6
In Progress 1
In Review 1
Done 1
Start here: Add your team's work
Due date
Aug 30, 2026
SCRUM-1
Connect your coding agent to Jira
Story 3.2: Complete Tool Return
Parent
Epic 3: Returns & Damage Tracking
SCRUM-15
Story 3.1: Log Damage Assessment
Parent
Epic 3: Returns & Damage Tracking
SCRUM-14
Story 2.2: Enforce Loan Duration Limits
Parent
Epic 2: Checkout & Deposit Manag...
SCRUM-13
Create



Lab 2 – Sprint Reflection

Community Tool & Equipment Library | PES1UG24CS421 | Problem Statement #52

Backlog Summary

4 Epics, 8 User Stories, 40 total story points (Fibonacci scale). Sprint 1 pulled in 6 of the 8 stories (29 of 40 points): SCRUM-10, 11, 12, 13, 14, and 15. SCRUM-16 and SCRUM-17 (both under Epic 4: Overdue & Access Control) were left in the backlog. By the time of the Active Sprint screenshot, SCRUM-13 (Enforce Loan Duration Limits, 8 pts) had reached Done, SCRUM-14 (Log Damage Assessment, 5 pts) was In Review, SCRUM-15 (Complete Tool Return, 3 pts) was In Progress, and SCRUM-10, 11, 12 (13 pts combined) remained in To Do.

1. Did your estimations reflect the actual effort?

Partially. The story that reached Done first, SCRUM-13 (8 points), was the highest-weighted story in the sprint and involved conditional logic across tool category and loan duration — its point value matched the work it represented. The two Epic 3 stories landed in different stages in a way that also tracked their point split: SCRUM-14 (Log Damage Assessment, 5 pts, involving a damage-status field plus photo evidence) reached In Review, while SCRUM-15 (Complete Tool Return, 3 pts, a simpler status flip) reached In Progress — the smaller story needed less

work to get moving, as expected. What the estimates didn't predict was completion order: two lower-weighted stories in Epic 1 (3 and 5 points) sat untouched in To Do while a heavier 8-point story in Epic 2 was finished. That suggests which story we picked up first mattered as much as its size — point value predicts effort, not sequencing.

2. Was your backlog well-prioritized?

Mostly, with one clear gap. Every story that made progress in Sprint 1 (SCRUM-13, 14, and to a lesser extent 15) was High priority, which is the outcome you'd want — the highest-priority work moved first. The gap is Epic 4 (Overdue & Access Control): SCRUM-16, the High-priority story that blocks overdue members from checking out more tools, never made it into Sprint 1 at all, while lower-priority stories from other epics did. Since Epic 4 is what actually protects the shared equipment pool from being monopolized by overdue members, leaving its core story out of the first sprint is a real prioritization miss — it should be one of the first stories pulled into Sprint 2, ahead of the remaining Medium-priority stories still sitting in To Do.

3. How did your simulated sprint align with your plan?

6 of 8 backlog stories (29 of 40 points) were committed to Sprint 1. Of that committed work, roughly 28% reached Done (8 pts), another 28% was actively in flight across In Progress and In Review (8 pts combined), and about 45% (13 pts) hadn't been started. That's a realistic spread for a short simulation — real sprints rarely finish everything that's committed, and having work genuinely distributed across all four board columns is a more honest sprint snapshot than artificially dragging every card straight to Done would have been. If anything, committing 29 of 40 total backlog points to a single sprint was ambitious; a real team would likely have scoped Sprint 1 closer to 15–20 points and left Epic 4 for Sprint 2 by design rather than by accident.

4. What insights did the burndown chart give about your team's capacity?

The chart was captured right after Sprint 1 started, showing only the "Today" marker at Aug 26 with the remaining-work line still flat — no drop was visible yet, even though SCRUM-13 had already reached Done on the board by that point. This is an artifact of timing rather than a real signal about capacity: Jira's burndown chart updates on a daily cadence rather than instantly as cards move, so a chart pulled minutes into a sprint won't yet reflect same-day progress. The real insight here is procedural: to get a burndown chart that actually shows a meaningful slope for the demo, the chart should be re-pulled after the sprint has run across at least one day boundary — at that point it should show a visible drop reflecting the Done story, rather than the flat line seen in this first capture.

JIRA WORKSPACE LINK -
https://sanjanaaithal28.atlassian.net/jira/software/projects/SCRUM/boards/1/backlog?epics=visible&atlOrigin=eyJpIjoiM2Y2MmU4ZGNlNTA3NGFkOThkNDU0ODdmNTYwZTBhMzciLCJwIjoiaiJ9
